Static Pressure Test Locations

Client :_____

Tested by:		Date:
Audit: ☐	WX: ☐ QCI: ☐	

Test Location	Pressure	Units (Circle One)
Ⓐ		Pa/"WC
Ⓑ		Pa/"WC
Ⓒ		Pa/"WC
Ⓓ		Pa/"WC

Pressure Drop Over Coil (Subtract) or N/A ☐

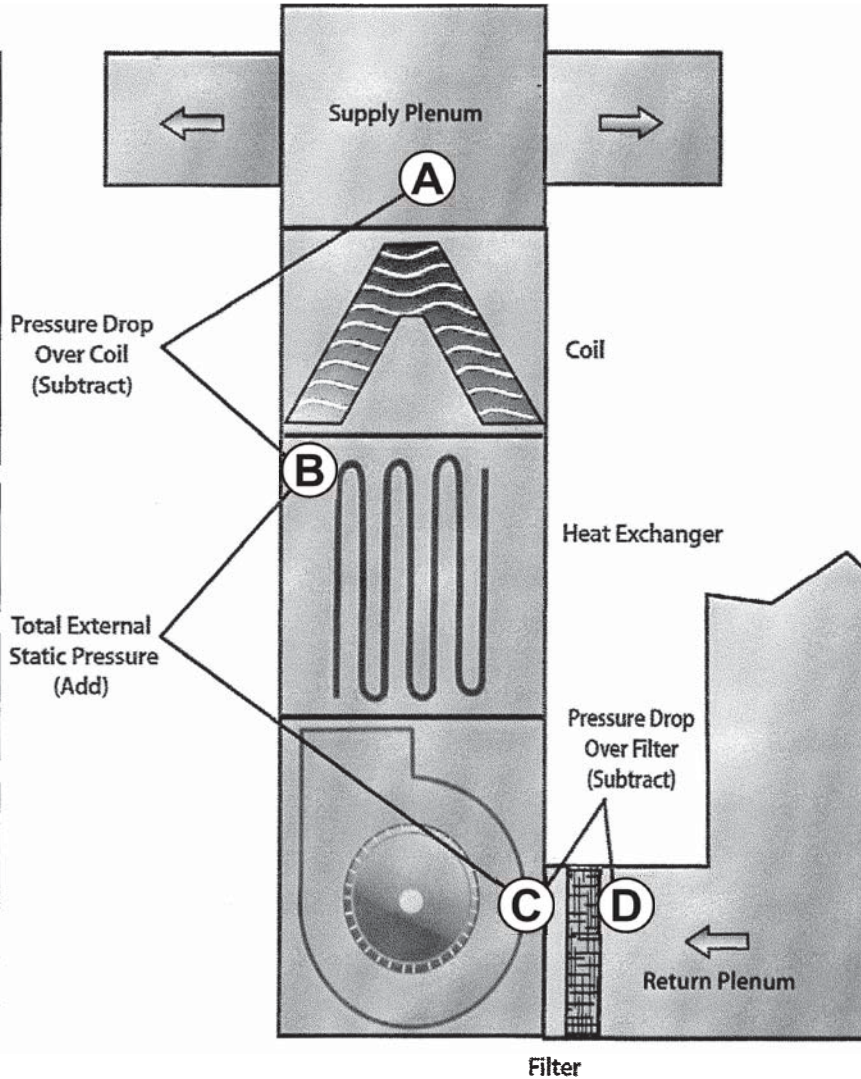Ⓐ ____ - Ⓑ _____ = _____ Pa/"WC

Pressure Drop Over Filter (Subtract)

Ⓒ ____ - Ⓓ _____ = _____ Pa/"WC

Total External Static Pressure (Add)

Ⓑ ____ + Ⓒ _____ = _____ Pa/"WC

Recommended Actions:

_____

_____

Supply Plenum

Ⓐ

Pressure Drop Over Coil (Subtract)

Coil

Ⓑ

Heat Exchanger

Total External Static Pressure (Add)

Pressure Drop Over Filter (Subtract)

Ⓒ Ⓓ

Return Plenum

Filter

High limit switches may be removed and pressure taken at that location.
Disconnect power before removing the switch.
